




MOODY METHODIST CHURCH

2021 MOODY STEEPLE CLADDING REPAIRS

WEEKLY FIELD REPORT No. 01

WEEK OF 1/18/2021

Weekly Weather

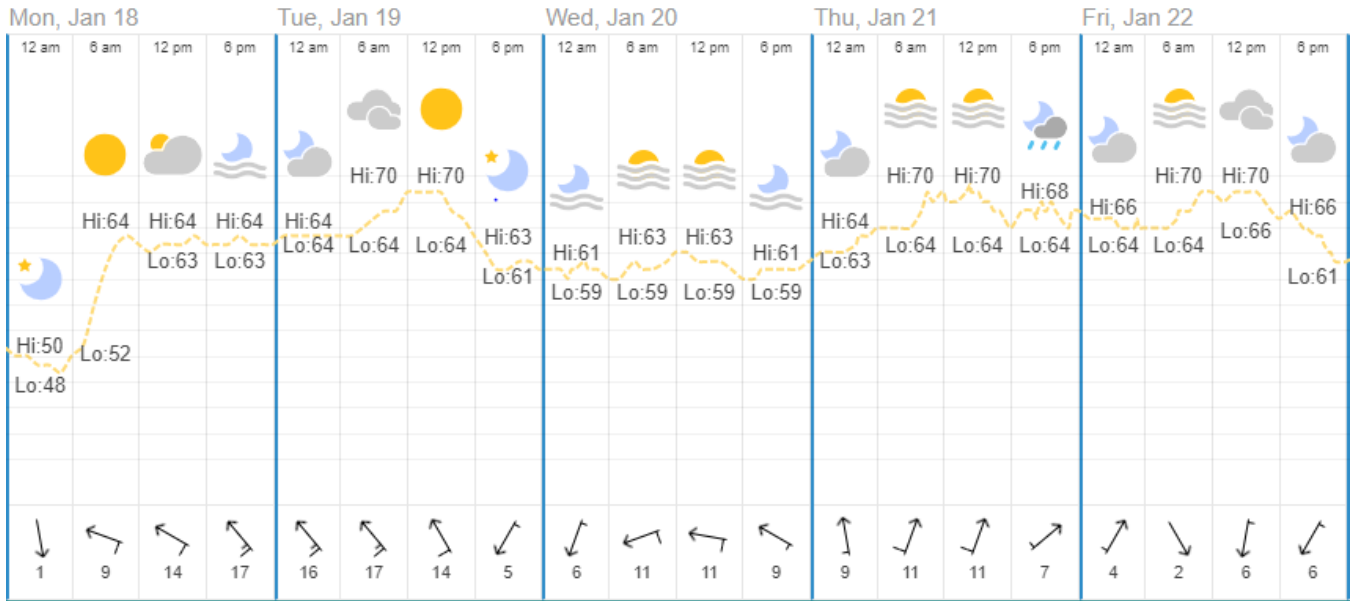

Date: Monday, January 18, 2021

On Site: Coltzer Company, LLC
Betco Scaffolds

Temperature – Low/High (°F): 48/64

Rain (Total Inches): 0.00"

Max Wind Speed(mph): 17 SE

Field Note: **Comments & Photographs:**

01 18-01 *Coltzer Company, LLC* on site to observe steeple repairs progress.

01 18-02 *Betco Scaffolds* begins erecting scaffolding on the south side of the sanctuary. (*see photo01-06*)





Photo01: Preparing for Scaffolding



Photo02: Scaffolding Unloaded from the Truck



Photo03: Scaffolding Being Assembled



Photo04: Scaffolding Being Assembled



Photo05: Scaffolding Being Assembled



Photo06: Scaffolding Material Laid Out

Date: Tuesday, January 19, 2021

On Site: Coltzer Company, LLC
Betco Scaffolding

Temperature – Low/High (°F): 61/70

Rain (Total Inches): 0.00

Max Wind Speed(mph): 17 SE

Field Note: **Comments & Photographs:**

01 19-01 *Coltzer Company, LLC* on site to observe steeple repairs progress.

01 19-02 *Betco Scaffolding* continues erecting scaffolding on the south side of the sanctuary. (*see photo07-10*)



Photo07: Scaffolding Being Assembled



Photo08: Scaffolding Being Assembled



Photo09: Scaffolding Being Assembled



Photo10: 53rd Street View of Scaffolding

Date: Wednesday, January 20, 2021

On Site:	Coltzer Company, LLC	Temperature – Low/High (°F):	59/63
	Betco Scaffolding	Rain (Total Inches):	0.00
		Max Wind Speed(mph):	11 E

Field Note: **Comments & Photographs:**

01 20-01 *Coltzer Company, LLC* on site to observe steeple repairs progress.

01 20-02 *Betco Scaffolding* continues erecting scaffolding on the south side of the sanctuary. (*see photo11-14*)



Photo11: Scaffolding Being Assembled



Photo12: Scaffolding Being Assembled



Photo13: Lift Brought in to Help Assemble Scaffolding

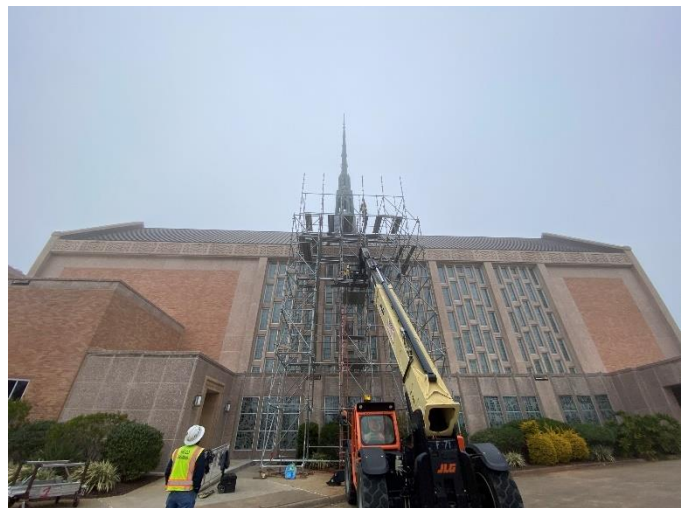


Photo14: Lift Used to Carry Up Scaffolding Equipment

Date: Thursday, January 21, 2021

On Site: Coltzer Company, LLC

Temperature – Low/High (°F): 63/70

Rain (Total Inches): 0.00"

Max Wind Speed(mph): 11 SSW

Field Note: Comments & Photographs:

01 21-01 *Coltzer Company, LLC* on site to observe steeple repairs progress.

01 21-02 *Betco Scaffolding* continues erecting scaffolding on the south side of the sanctuary. Scaffold supports are placed on the roof of the sanctuary. (*see photo15-18*)



Photo15: Scaffold Supports on Foam and Plywood



Photo16: Scaffolding Being Assembled Above Roof



Photo17: Scaffold Supports Being Placed on Roof of Sanctuary



Photo18: Scaffold Supports Being Placed on Roof of Sanctuary

Date: Friday, January 22, 2021

On Site:	Coltzer Company, LLC	Temperature – Low/High (°F):	46/63
	Mann's Carpentry	Rain (Total Inches):	0.00
	RB Hash	Max Wind Speed(mph):	17 S

Field Note: **Comments & Photographs:**

01 22-01 ***Coltzer Company, LLC*** on site to observe steeple repairs progress.

01 22-02 ***Betco Scaffolding*** continues erecting scaffolding on the south side of the sanctuary. Scaffold supports are placed on the roof of the sanctuary. Chain link fence is placed around the scaffolding. (*see photo19-22*)



Photo19: Scaffolding Being Assembled on Roof



Photo20: Scaffolding Assembled on Roof



Photo21: Scaffolding Assembled on Roof



Photo22: Chain Link Fence Around Scaffolding

DISTRIBUTION LIST

NAME	REPRESENTING	PHONE NUMBER	E-MAIL
Bill Coltzer	Coltzer Company, LLC	409-740-0090	bcoltzer@z6consulting.com
Lidija Bikova	Zero/Six Consulting, LLC	409-740-0090	LBikova@z6consulting.com
Richard Parks	Coltzer Company, LLC	470-314-2821	rparks@z6consulting.com
Sam Caminade	Moody Church	409-771-7785	sam@moody.com
Bryan Hash	R.B. Hash Roofing		rbh@rbhash.com
John Garza	R.B. Hash Roofing		jgarza@rbhash.com
Justin Wenner	Betco Scaffolding		justin.wenner@scaffold.com
Steve Grimes	Betco Scaffolding		steve.grimes@scaffold.com

The preceding represents Coltzer Company's understanding of the principal matters discussed and/or observed. Written comments with regard to the content of this report should be received by Coltzer Co. within three days from date of issue. After that date, these notes shall stand as a final accounting of the items discussed and/or observed.
