




# MOODY METHODIST CHURCH

## 2021 MOODY STEEPLE CLADDING REPAIRS

### WEEKLY FIELD REPORT NO. 04

### WEEK OF 2/08/2021

#### Weekly Weather

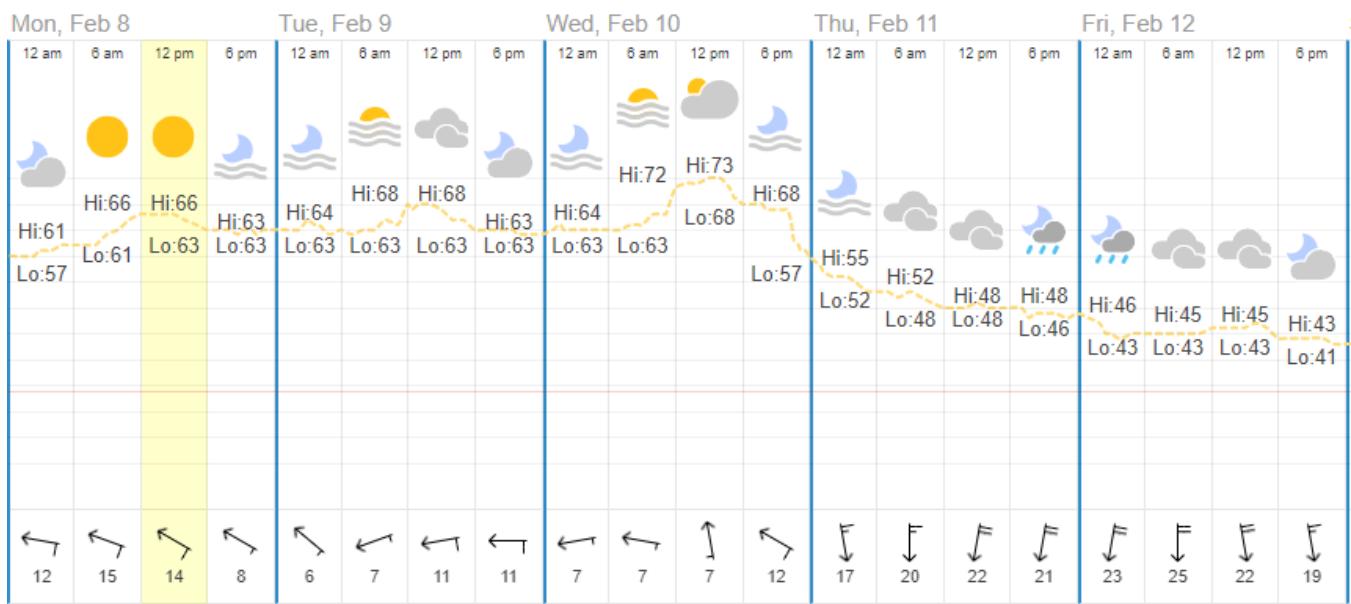

Date: Monday, February 08, 2021

On Site:	Coltzer Company, LLC RB Hash	Temperature – Low/High (°F):	57/66
		Rain (Total Inches):	0.00"
		Max Wind Speed(mph):	15 ESE
Field Note:	Comments & Photographs:		
02 08-01	<i>Coltzer Company, LLC</i> on site to observe steeple repairs progress.		
02 08-02	RB Hash continues removing old copper cladding from next tier of the steeple. RB Hash also continues applying waterproofing membrane on the steeple. ( <i>See photo01-04</i> )		



Photo01: Overview of Work in Progress



Photo02: Removed Copper Cladding



Photo03: Exposed Wood Underneath Copper Cladding



Photo04: Waterproof Membrane Applied on Next Tier

**Date: Tuesday, February 09, 2021**

<b>On Site:</b>	Coltzer Company, LLC RB Hash	<b>Temperature – Low/High (°F):</b>	63/68
		<b>Rain (Total Inches):</b>	0.00
		<b>Max Wind Speed(mph):</b>	10 NE

**Field Note: Comments & Photographs:**

**02 09-01** *Coltzer Company, LLC* on site to observe steeple repairs progress.

**02 09-02** *RB Hash* continues removing copper cladding on the next tier of the steeple. (see photo05-07)



Photo05: Steel Beams Beneath the Copper Cladding



Photo06: More Copper is Removed



Photo07: Overview of Work in Progress

**Date: Wednesday, February 10, 2021**

On Site:	Coltzer Company, LLC RB Hash	Temperature – Low/High (°F):	54/64
		Rain (Total Inches):	0.00
		Max Wind Speed(mph):	16 SE

**Field Note:** **Comments & Photographs:**

**02 10-01** *Coltzer Company, LLC* on site to observe steeple repairs progress.

**02 10-02** *RB Hash* continues removing copper cladding from the upper tier of the steeple. *(see photo08-09)*



Photo08: Overview of Work in Progress



Photo09: Copper Cladding Removed from Upper Level of Steeple

**Date: Thursday, February 11, 2021**

On Site:	N/A	Temperature – Low/High (°F):	46/55
		Rain (Total Inches):	0.20"
		Max Wind Speed(mph):	22 N

**Field Note:** **Comments & Photographs:**

**02 11-01** *Coltzer Company, LLC* was not on site due to rain and heavy winds.

**Date: Friday, February 12, 2021**

On Site:	N/A	Temperature – Low/High (°F):	41/46
		Rain (Total Inches):	0.56"
		Max Wind Speed(mph):	25 N

**Field Note:** **Comments & Photographs:**

**02 12-01** *Coltzer Company, LLC* was not on site due to rain and heavy winds.

**DISTRIBUTION LIST**

NAME	REPRESENTING	PHONE NUMBER	E-MAIL
Bill Coltzer	Coltzer Company, LLC	409-740-0090	<a href="mailto:bcoltzer@z6consulting.com">bcoltzer@z6consulting.com</a>
Lidija Bikova	Zero/Six Consulting, LLC	409-740-0090	<a href="mailto:LBikova@z6consulting.com">LBikova@z6consulting.com</a>
Richard Parks	Coltzer Company, LLC	470-314-2821	<a href="mailto:rparks@z6consulting.com">rparks@z6consulting.com</a>
Sam Caminade	Moody Church	409-771-7785	<a href="mailto:sam@moody.com">sam@moody.com</a>
Bryan Hash	R.B. Hash Roofing		<a href="mailto:rbh@rbhash.com">rbh@rbhash.com</a>
John Garza	R.B. Hash Roofing		<a href="mailto:jgarza@rbhash.com">jgarza@rbhash.com</a>
Justin Wenner	Betco Scaffolding		<a href="mailto:justin.wenner@scaffold.com">justin.wenner@scaffold.com</a>
Steve Grimes	Betco Scaffolding		<a href="mailto:steve.grimes@scaffold.com">steve.grimes@scaffold.com</a>

*The preceding represents Coltzer Company's understanding of the principal matters discussed and/or observed. Written comments with regard to the content of this report should be received by Coltzer Co. within three days from date of issue. After that date, these notes shall stand as a final accounting of the items discussed and/or observed.*
