




MOODY METHODIST CHURCH

2021 MOODY STEEPLE CLADDING REPAIRS

WEEKLY FIELD REPORT No. 03

WEEK OF 2/01/2021

Weekly Weather

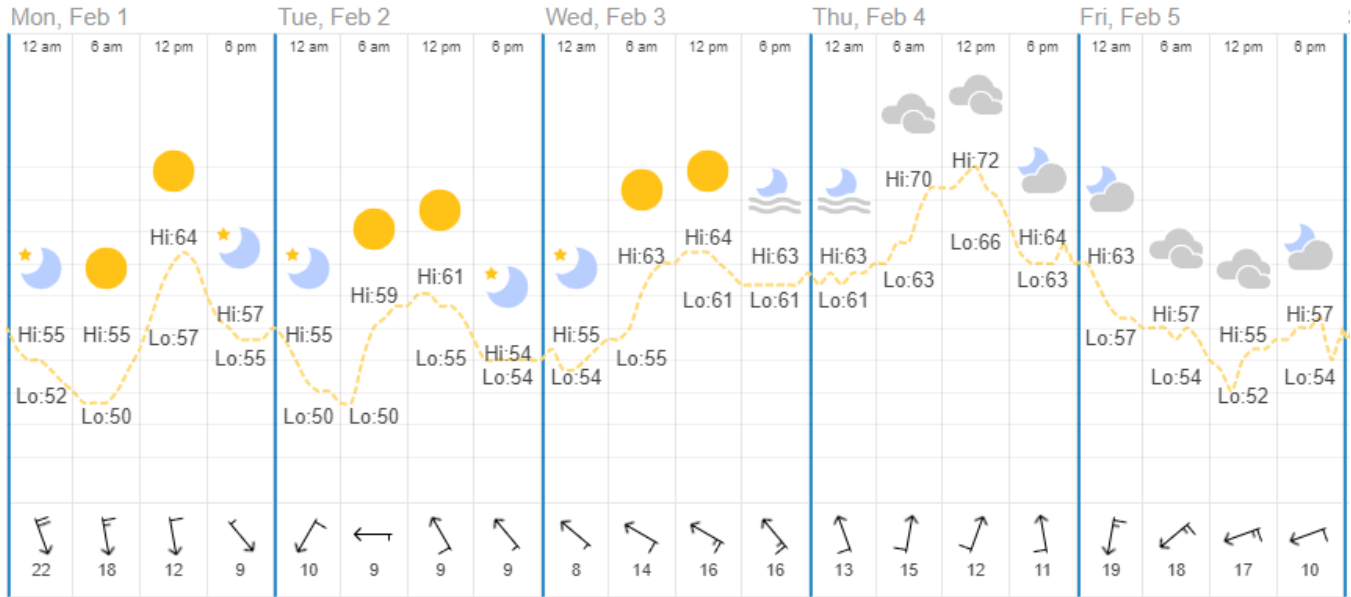

Date: Monday, February 01, 2021

On Site: Coltzer Company, LLC
RB Hash

Temperature – Low/High (°F): 50/64

Rain (Total Inches): 0.00"

Max Wind Speed(mph): 22 NNW

Field Note: Comments & Photographs:

02 01-01 *Coltzer Company, LLC* on site to observe steeple repairs progress.

02 02-02 *RB Hash* begins removing old copper cladding from the steeple. Speakers for the electronic bell are removed, and measurements of the underlying wood are taken. RB Hash also begins applying waterproofing membrane at the first level of the steeple. (See photo01-06)





Photo01: RB Hash Begins Removing Copper Cladding



Photo02: Old Sealant is Scraped Away and Copper Removed



Photo03: Speakers are Removed



Photo04: Copper Cladding is Removed

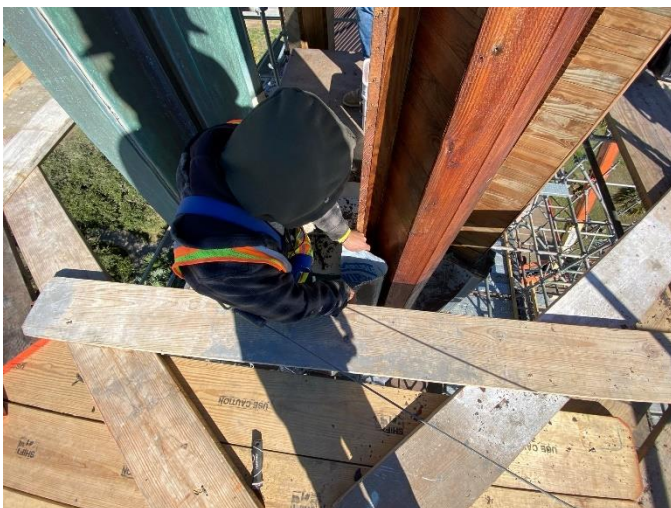


Photo05: Waterproof Membrane Applied at Steeple

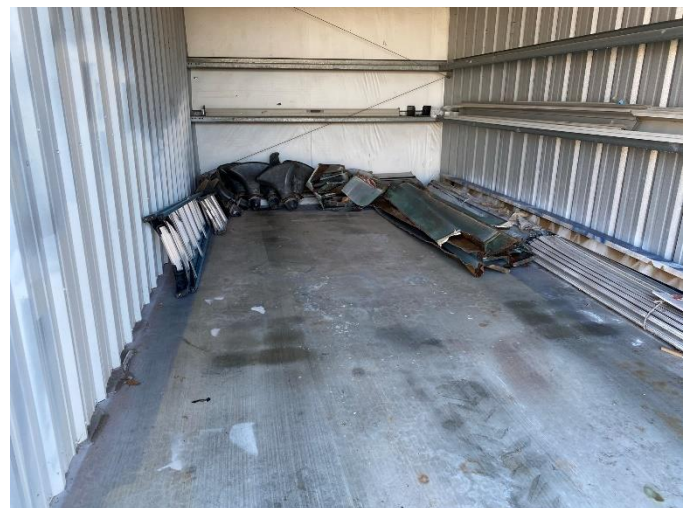


Photo06: Old Copper and Speakers are Placed in Storage on Site

Date: Tuesday, February 02, 2021

On Site: Coltzer Company, LLC
RB Hash

Temperature – Low/High (°F): 50/64

Rain (Total Inches): 0.00

Max Wind Speed(mph): 10 NE

Field Note: Comments & Photographs:

02 02-01 *Coltzer Company, LLC* on site to observe steeple repairs progress.

02 02-02 *RB Hash* continues applying waterproofing membrane around the first level of the steeple. (*see photo07-10*)



Photo07: Copper Cladding is Brought Down



Photo08: Waterproofing Product Delivered



Photo09: Waterproofing Applied

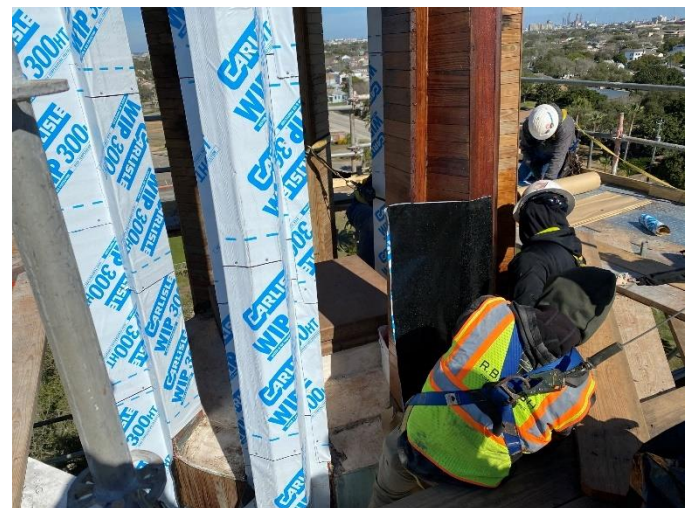


Photo10: Waterproofing Applied

Date: Wednesday, February 03, 2021

On Site: Coltzer Company, LLC
RB Hash

Temperature – Low/High (°F): 54/64

Rain (Total Inches): 0.00

Max Wind Speed(mph): 16 SE

Field Note: **Comments & Photographs:**

02 03-01 *Coltzer Company, LLC* on site to observe steeple repairs progress.

02 03-02 *RB Hash* begins removing copper cladding from the base of the steeple. (*see photo11-14*)



Photo11: Copper Cladding Removed from Base of Steeple

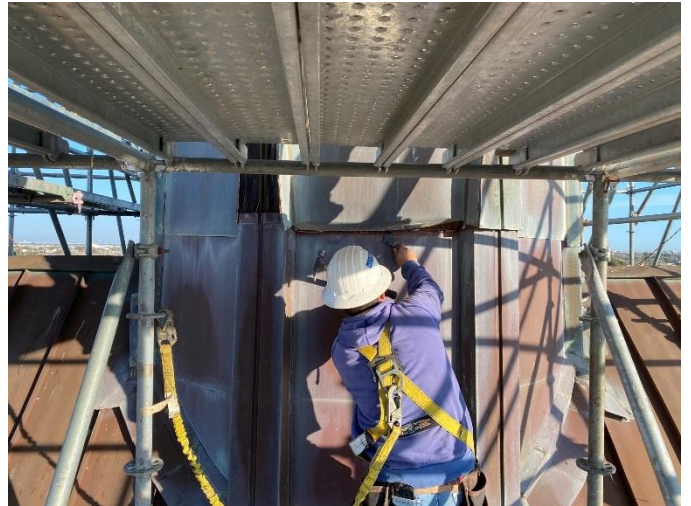


Photo12: Copper Cladding Removed from Base of Steeple



Photo13: Exposed Wood After Removing Copper

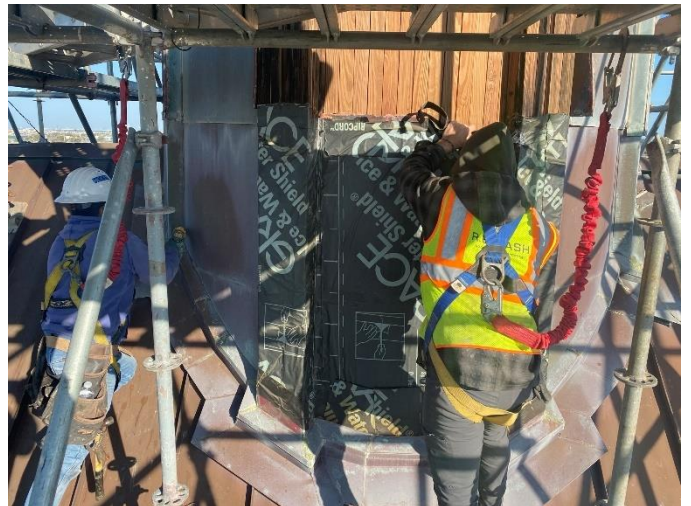


Photo14: Old Membrane is Removed

Date: Thursday, February 04, 2021

On Site: Coltzer Company, LLC
RB Hash

Temperature – Low/High (°F): 61/72

Rain (Total Inches): 0.00"

Max Wind Speed(mph): 15 S

Field Note: **Comments & Photographs:**

02 04-01 *Coltzer Company, LLC* on site to observe steeple repairs progress.

02 04-02 *RB Hash* continues removing copper cladding and applying waterproof membrane. (*see photo15-21*)



Photo15: Waterproof Membrane Applied



Photo16: Copper Cladding Removed at Base of Steeple



Photo17: Copper Top Removed from Base of Steeple

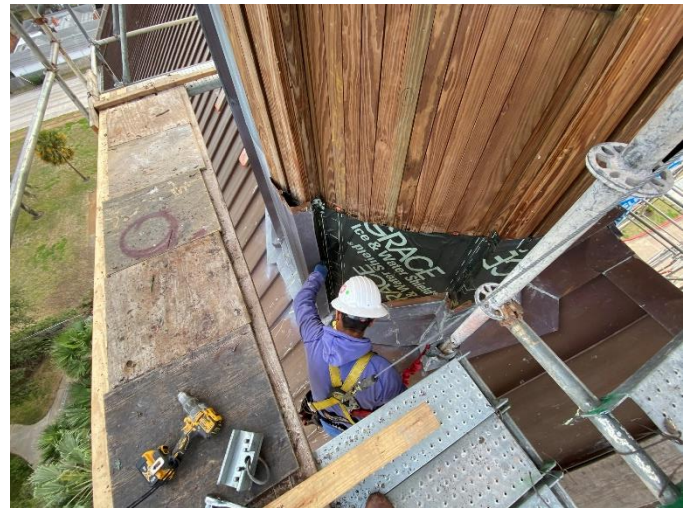


Photo18: Old Membrane Removed



Photo19: Wooden Top Removed



Photo20: Wooden Top Removed



Photo21: New Wood is Cut to Replace Old Wood

Date: Friday, February 05, 2021

On Site: Coltzer Company, LLC

Temperature – Low/High (°F): 52/63

Rain (Total Inches): 0.00

Max Wind Speed(mph): 19 N

Field Note: Comments & Photographs:

02 05-01 *Coltzer Company, LLC* on site to observe steeple repairs progress

02 05-02 *RB Hash* continues removing copper cladding and applying waterproof membrane. (see photo22-25)



Photo22: Removed Copper Cladding



Photo23: Waterproof Membrane Applied Around Steeple



Photo24: Waterproof Membrane Applied



Photo25: Overview of Progress

DISTRIBUTION LIST

NAME	REPRESENTING	PHONE NUMBER	E-MAIL
Bill Coltzer	Coltzer Company, LLC	409-740-0090	bcoltzer@z6consulting.com
Lidija Bikova	Zero/Six Consulting, LLC	409-740-0090	LBikova@z6consulting.com
Richard Parks	Coltzer Company, LLC	470-314-2821	rparks@z6consulting.com
Sam Caminade	Moody Church	409-771-7785	sam@moody.com
Bryan Hash	R.B. Hash Roofing		rbh@rbhash.com
John Garza	R.B. Hash Roofing		jgarza@rbhash.com
Justin Wenner	Betco Scaffolding		justin.wenner@scaffold.com
Steve Grimes	Betco Scaffolding		steve.grimes@scaffold.com

The preceding represents Coltzer Company's understanding of the principal matters discussed and/or observed. Written comments with regard to the content of this report should be received by Coltzer Co. within three days from date of issue. After that date, these notes shall stand as a final accounting of the items discussed and/or observed.
